



ArcaScience

Seek less, discover better

Fixing Meeting

Fixing Meeting

THURSDAY 02/04/2026

Week 08 of 12

O1

AT RISK

O2

AT RISK

O3

BEHIND

Status: ON TRACK / AT RISK / BEHIND

Format & Purpose

Meeting Structure

Cadence: Every Thursday, 60 minutes

Attendees: whole team

Format: One section = one slide, optimized for screen-sharing or projection

Core Objective

Full-team visibility on weekly objective achievement, risk identification, and tactical problem-solving. Each objective owner reports on what shipped, what's at risk, and what requires immediate attention.

This is an operational check-in focused on execution velocity, quality metrics, and cross-functional dependencies. We move fast, stay honest, and leave with a clear action plan.

Quarter Progress Overview

WEEK 8 / 12

We are tracking our progress through the quarter with clear visibility into elapsed time and objective health. This snapshot shows where we stand across all three objectives and helps us identify early warning signs before they become blockers.



Quarter Elapsed

Week 8 of 12 weeks completed

Objective Health Summary

O1 Platform	G/Y/R	11 / 14
O2 Disease	G/Y/R	0 / 6
O3 Revenue	G/Y/R	0 / 6

Key Performance Indicator

Total KRs on track: 11 / 26

Success rate: / %

Our target is maintaining at least 85% of key results on track throughout the quarter. Any objective falling below 70% triggers immediate escalation and resource reallocation discussions.

O1: BRA Platform

STATUS: Y

Owners: Charbel (Product) · Jeff (CTO) · Vassili (Clinical)

The BRA Platform objective focuses on delivering core product functionality, ensuring system reliability, and maintaining quality standards. This week's report covers shipped features, work in progress, and any blockers preventing forward momentum.



01: What We Shipped

01. Shipped This Week

1. **Spec for cache, shared / private data** — Anne-C, Charbel, JF
2. **Step-1 Data: onboarding LLM-as-a-judge** — Théo, Natalia, Dimitri
3. **Step-4-5 webUI: deploy in staging (fake data)** — TSH / Fayez
4. **Funct/Tech spec for steps-6 staying on budget** — Clarisse / Fayez / JF / TSH
5. **Infra: SpotInstance - Ons**
6. **Tools: Sentry to Jira**

03. Blocked

1. **Step-3 waits for the progress of steps-1 and step-2**
2. **lack of (internal/external) people for LLM reviewer**
3. **lack of people for LLM as a judge.**

02. In Progress

1. **Step-1 Dags Industrialisation & deployment** — Anne-C
2. **Step-1 Data: LaaJ 1st prompt validation** — Théo / Natalia / Dimitri
3. **Step-2 Development** — Praise
4. **Step-6 webUI deploy in staging (fake data)** — TSH / Fayez
5. **Funct/Tech spec for steps-7 + notification flow budget driven** — Clarisse / Fayez / JF / TSH
6. **Infra: Autoscaling - Ons**
7. **MLOps tools deployment**
8. **annoation for LLM as a judge**

O1: Key Results Dashboard

KR	Key Result Area	Owner		Actual	Target	%	Spec Funct/Data	Spec Tech	Mocked service	1rst implem.	Usable Implem	Integrated in App
KR1.1a	WebbApp - Main Stories deployed and testable	App-Team		34	60	56,7%	Spec Funct/Data	Spec Tech	Mocked service	1rst implem.	Usable Implem	Integrated in App
KR1.5a	Code coverage (2/5 prj actually)	App-Team Data-Team		91,75	80	114,7%						
KR1.5b	Critical/Major bugs	App-Team Data-Team		0	0	100,0%						
KR1.1b	Active users/companies	App-Team Sales-Team		0	5	0,0%						
KR1.1B	Step 0 - "Config" - (WebOnly)	App-Team Data-Team		3	3	100,0%	✓	✓				✓
KR1.2	Step 1 - "Contexte"	App-Team Data-Team		5	6	83,3%	✓	✓	✓	✓		✓
KR1.3	Step 2 - "B&R outcomes indent"	App-Team Data-Team		4	6	66,7%	✓	✓	✓			✓
KR1.4	Step 3 - "Analysis"	App-Team Data-Team		4	6	66,7%	✓	✓	✓			✓
KR1.1c	Step 4 - "Customization" - (WebOnly)	App-Team Data-Team		3	3	100,0%	✓	✓				✓
KR1.1	Step 5 - "Weighting" - (WebOnly)	App-Team Data-Team		1	1	100,0%						✓
KR1.1d	Step 6 - "Display" - (WebOnly)	App-Team Data-Team		2	3	66,7%	✓	✓				□
KR1.1e	Step 7 - "Delivery" - (WebOnly)	App-Team Data-Team		2	3	66,7%	✓	✓				□
KR1.5c	Platform uptime last 30 days	Devops-Team		100	99	101,0%						
KR1.5d	Deployment speed including image Building	Devops-Team		45	10	30,0%						
KR1.5e	APM instrumentation	Devops-Team		25	100	25,0%						
						77,0%						



Dossier privé



The background features a light blue gradient with several large, semi-transparent white and light blue circles of varying sizes. A faint, stylized world map is visible in the upper right quadrant. The text "01 & 02 Planning" is positioned on the left side, overlaid on one of the large circles.

01 & 02 Planning

Not Yet – Credibility & Performance Trends

Credibility Assessment

Are BRA outputs trustworthy this week? [YES / NO]

Top Issues

1. _____
2. _____
3. _____

Noise Analysis

False positives count: ____

Worst case example:

F1 Score Trend Analysis

Risk/Safety	____%	____%	[▲/■/ ▼]
Efficacy	____%	____%	[▲/■/ ▼]

Calibration vs Reference Datasets

Tests passed: ____ / ____

Pass rate: ____%

We calibrate against established reference datasets to ensure our models maintain accuracy across diverse clinical scenarios and patient populations.



O2: Disease-Specific Platform

STATUS: Y

Owner: Vassili

The disease-specific platform objective extends our core BRA capabilities to targeted therapeutic areas. This work involves structuring specialized datasets, validating against clinical standards, and building relationships with key opinion leaders who can validate our approach.

O2: Progress Report

Done This Week

1. integration of conception gaps result in the final documentation
2. Gaps per disease analysis
3. Kick off LLM as a reviewer (with O1)
4. Finalizing Medical KOL SOP and contract (with Julie)

In Progress

1. Defining cut offs and patient subgroups based on RA disease drivers
2. RA US KOL reminders
3. Follow up on contracts to onboard KOLs

Blocking

Disease-specific work requires close coordination between clinical expertise, data engineering, and platform development. Blockers in this area often involve access to specialized datasets, expert validation bottlenecks, or technical integration challenges with the core platform.

Therapeutic Axis Tracker

We track progress across multiple therapeutic axes simultaneously, measuring dataset readiness, validation completion, platform integration, and demo preparation. Each axis moves through a structured pipeline from initial structuring through final validation.



Dataset Structured KR1

Validation KR2


Platform Integration KR3

Demo Ready KR3

This standardized pipeline ensures consistent quality across all therapeutic areas while allowing parallel development. Each axis has clear milestones and validation gates before progressing to the next stage.

OKR1 and OKR2 Dependencies- Updated Plan

We track progress across multiple therapeutic axes simultaneously, measuring dataset readiness, validation completion, platform integration, and demo preparation. Each axis moves through a structured pipeline from initial structuring through final validation.

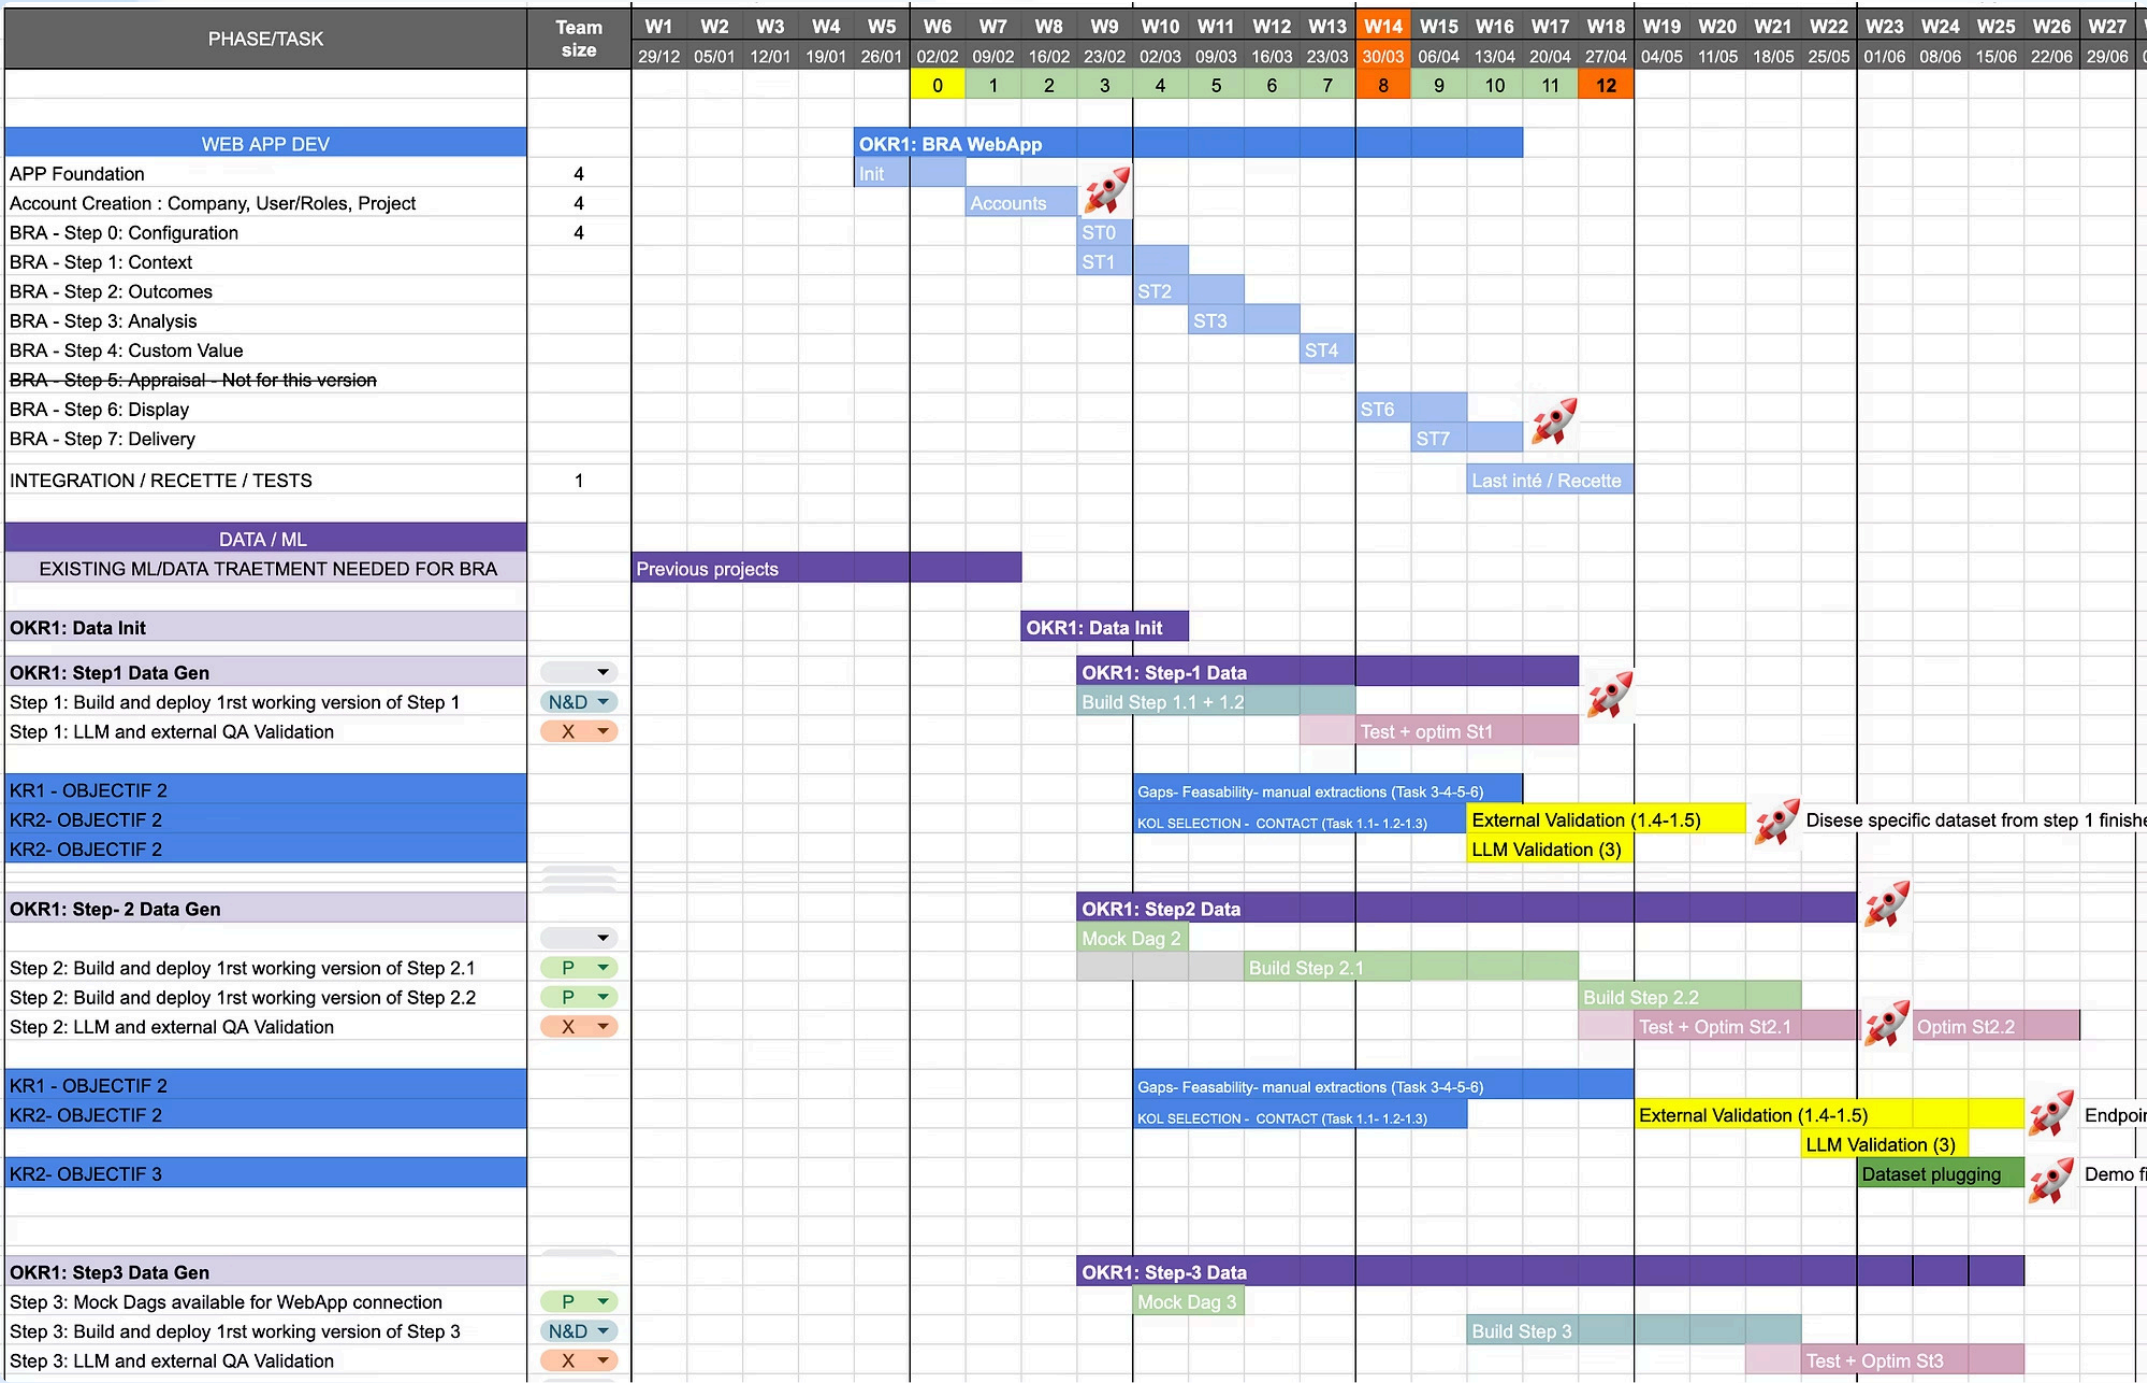

This standardized pipeline ensures consistent quality across all therapeutic areas while allowing parallel development. Each axis has clear milestones and validation gates before progressing to the next stage.

Axis 1 & 2: Detailed Status

Axis 1: [Name]

Dataset structured	0%
External validation	0 / 4
Internal validation	Reported to Q2
LLM validation	0 / 4
Platform integration	0%
Demo ready	[NA]

Axis 2: [Name]

Dataset structured	0%
External validation	0/ 4
Internal validation	Reported to Q2
LLM validation	0 / 4
Platform integration	0%
Demo ready	[NA]

Axis 3 (Stretch Goal): [Name]

Go/No-go decision: __ | If go, completion: __%

KOL Engagement Progress

Contacted: 0 / 5 | Sessions completed:0 | Sessions scheduled: 0

O3: Revenue Engine

STATUS: R

Owner: CEO

New BM - New Pricing - 2 proposal made

Pipeline Snapshot

Key Metrics vs Targets

ARR closed	\$0k	\$500k
New logos	0	5
Expansions	0	1
Pipeline qualified	\$1,116,250== > \$1,225,250.	\$2,355,000

- **Weighted forecast S2+: \$1,026k** (vs ton ancien \$1,016k - léger delta, probablement dû à l'ajout d'Osivax à \$50k en S4)
- **Best Case est maintenant à 16 deals / \$1,065k** (vs tes 13 deals / \$1,015k - 3 deals supplémentaires: Osivax \$50k, Pierre Fabre \$10k, et Edetek/CG \$0)
- **Commit reste stable à \$160k** (2 deals quasi acquis)

Pipeline Health Indicators

- Coverage ratio: **2.45x** (target: 5x)
- Win rate: 0% (target: 20%)
- Avg pilot sales cycle: 30 days (target: <60)
- Avg sales cycle: 180 days (target: <180)
- Avg upsell cycle: 60 days (target: <60)

Revenue Forecast

- **Commit:** \$160k, 2 deals - Paris Brain Institute \$100k + ICON DSUR \$60k
- **Weighted Best Case (S3-S5):** \$648k (16 deals)
- **Upside (S1+S2):** \$3,640k, 163 deals
- **Weighted forecast (S3+):** \$800k

CEO Revenue Hours This Week: 15<25

Target: 12-15h weekly minimum

Deal Funnel Distribution

Our funnel shows the distribution of opportunities across each stage from initial target through closed-won. Healthy funnel shape requires sufficient volume at each stage to support our revenue targets, with natural conversion rates between stages.



- ☐ **Funnel health check:** We need 5x coverage at top of funnel to hit targets. Any stage with <2 deals triggers immediate prospecting acceleration.

Pipeline Tracker (Update Every Monday)

Active Deal Board

Deal #	Company	Stage	Tier	Therapeutic Axis	ACV	Champion	Last Contact	Next Action	Due Date	Forecast	Red Flags
1	Kymera	S_0	C	HS	\$50k	Neil	2.25, phone	FU in 2 weeks	3.11	Prospect	Smaller company
2	Sonoma	S_0	C	HS	\$50k	Josh	2.25, phone	FU in 2 weeks	3.11	Prospect	Multiple competing projects in pipeline
3	Zura	S_0	C	HS	\$50k	Gary	2.25, phone	FU in 2 weeks	3.11	Prospect	Smaller company
4	Avalo	S_0	C	HS	\$50k	Dino	2.25, phone	FU in 2 weeks	3.11	Prospect	Smaller company
5	AbbVie	S_0	-	HS/LNP	\$100k	Rahesh-Li Wang	03.02 email	FU in 1 week	03.09	Prospect	Therapeutic Type Unknown Interest
6	Observia	S_3	-	CRO	\$50k	Guillaume	3.4, demo	FU in 2 weeks	3.11	Prospect	CRO, not in HS
7	CSL	S_1	-	CRO	\$50k	Priyanka - Julia	03.03	FU in 2 weeks	03.17	Prospect	CRO
8	Sanofi	S_2	-	HS	\$10k	Multiple	Ongoing	FU in 2 weeks, secure next meeting	3.9	Qualified	Custom project - share the publication links
9	Roche	S0	A	/	\$250k	Ollivier Ottaviani/ Renato Pereira	Ongoing	S2 awaiting Move forward with other PSUR/DSUR Specific people in the company / ICSR need	03/12	Qualified	Has fired other company
10	Hyloris	S1	A	Cardio	\$100k	Steijn CEO / CFO	Ongoing	S2 next monday	03/10	Qualified	Potential multi-patho
11	Incyte	S1	B	HS	\$	Head of safety	Ongoing	S2 to be done	03/12	Qualified	Non-respondant
12	Transgene	S0	-		\$						
13	Asphalion	S1	C	Gen.	25k	Head of safety	ongoing	S2 to schedule	03/30	qualified	

Stage Summary (auto-calculate or fill manually)

Stage	Deals	Avec montant	Montant brut	Stage	Deals	Avec montant
Target Identified	138	57	\$2,510,000	Target Identified	138	57
Discovery Complete	25	22	\$1,130,000	Discovery Complete	25	22
Need Validated	5	3	\$210,000	Need Validated	5	3
Demo Delivered	9	9	\$580,000	Demo Delivered	9	9
Proposal Sent	2	2	\$275,000	Proposal Sent	2	2
Negotiation	0	0	\$0	Negotiation	0	0
To Be Launched	2	2	\$160,000	To Be Launched	2	2
TOTAL	181	95	\$4,865,000	TOTAL	181	95

Weekly Activity & Top Deals

This Week's Activity

- **Outbounds sent:** 16<34
- **Meetings held:** 4=4
- **Demos delivered:** 4>1
- **Proposals sent:** 0<2
- **Warm intros received:** /
- **Deals advanced:** /
- **Deals disqualified:** 0

Activity metrics drive pipeline velocity. We track both volume and quality, ensuring we're engaging the right prospects with appropriate messaging and moving deals forward efficiently.

Top 3 Deals (Closest to Close)

Top Deals (Closest to Close)

Deal #1 - Sanofi IHI V2 Stage: S4 (Proposal Sent) | Value: \$240k | Close: May 31 | Last activity: Mar 12 Next: Approval April

Deal #2 - Paris Brain Institute - NS-PARK Master Trial Stage: S6 (To Be Launched) | Value: \$100k | Close: Apr 30 | Last activity: Mar 26 Next: Contract execution, launch imminent

Deal #3 - Icon - Cassandra Stage: S3 (Demo Delivered) | Value: \$250k | Close: Mar 30 | Last activity: Jan 5 Next: Needs re-engagement, close date is in 4 days

Deal #4 - Hyloris Pharmaceuticals Stage: S3 (Demo Delivered) | Value: \$80k | Close: Mar 31 | Last activity: Mar 25 Next: Convert to proposal, close date in 5 days

Deal #5 - Biocodex PV/BRA Stage: S3 (Demo Delivered) | Value: \$70k | Close: Mar 27 | Last activity: Nov 26 Next: Re-engage urgently, close date is tomorrow

Deal #6 - ICON DSUR Stage: S6 (To Be Launched) | Value: \$60k | Close: Apr 30 Next: Lock in kick-off date

Deal #7 - Dillon Technologies Upsell Stage: S4 (Proposal Sent) | Value: \$35k | Close: Apr 30 | Last activity: Mar 24 Next: Retrieve decision



Red Flags & Risks

Early warning system for objective health. Each objective has specific gate criteria and milestones that must be met on schedule. Red flags indicate areas requiring immediate attention, resource reallocation, or escalation to leadership.

01 Platform Red Flags

TSH's budget overrun	Reevaluation of the budget after specs finalisation. Meeting Friday 06/03 11:00 AM to confirm we will not pay any extra.
Data validation delay incompatible with 2 Disease integration on time	Demo the platform without validation OR Start selling generic platform before specific ones
Implementation of acurated data for therapeutic vertical	Tackle shared / private Clients Data subject.
Step-3 delay based on previous steps delay	
Lack of ressources for LLM Validator	

Platform red flags focus on delivery velocity, quality trends, and system reliability. Missing any checkpoint triggers immediate investigation and corrective action planning. We don't wait for problems to compound.

O2 Disease & O3 Revenue Red Flags

O2 Disease-Specific Platform

Axes benchmarked (10) by Wk 2?	OK
Axes selected (2-3) by Wk 3?	[OK]
Gap analysis done by Wk 4?	[OK- late]
First dataset structured by Wk 7?	[late]
KOL contacts initiated by Wk 5?	[Early]
1 demo ready by Wk 10?	[Late]

O3 Revenue Engine

Pipeline coverage >2x? ==> being solved	! needs to accelerate ==> accelerated
Meetings >2/week?	starting to accelerate
Proposals outstanding >0 by Wk 5?	2 sent
Deals at S4+ >2 by Wk 6?	OK
ARR >\$0 by Wk 8?	OK
Avg deal size >\$80k?	OK

Triggered Flags This Week: ___

List all triggered flags: _____

Cross-Objective Issues & Dependencies

Value Chain Link Assessment

O1 → O2 link	[YES / NO]
O2 → O3 link	[YES / NO]
End result on track	[YES / NO]

Cross-Objective Issues

1. Validate Output for Therapeutic Vertical depend and output validation of each BRA steps
2. _____

Dependencies Blocking Progress

These represent work in one objective that's preventing progress in another. Resolving these dependencies is the highest priority for maintaining overall momentum.

From O1.2, 1.3, 1.4 → Blocks O[2.1]:
Small delays expected

From O[_] → Blocks O[_]:

Action Plan

Maximum 7 fix items for next week. Each has a clear owner and deadline. This is our commitment to resolving the most critical issues identified in this meeting. No vague action items—every fix is specific, measurable, and time-bound.

Fix Items for Next Week

1	Reevaluation of the budget after specs finalisation. Meeting Friday 06/03 11:00 AM to confirm we will not pay any extra.	01	Ongoing	06/03/2026
2	Reevaluation global planning for O1 & O2	O1 O2	Ongoing	??/03/2026
3	Validation resources lacking ==> research of freelance	O1	Ongoing	18/02/2026
4	_____	O_	_____	[Date]
5	_____	O_	_____	[Date]
6	_____	O_	_____	[Date]
7	_____	O_	_____	[Date]

Deferred Items & Decisions

Deferred Items

Acknowledged issues that won't be addressed this week due to prioritization or resource constraints. These remain visible for future planning but don't block current sprint execution.

-
- 1. Investor's relationship__
 - 2. _____
 - 3. _____

Decisions Made in This Meeting

Key decisions requiring documentation and team alignment. Each decision includes the decision maker to establish clear accountability.

Decided by: ____

Decided by: ____

Closing Assessment

Biggest Quality Risk Right Now

Step 1 to be dealt with to unblock rest of the Os. _____

Confidence in What We're Shipping

Are we confident? [YES / NO]

Escalation Status

Escalation meeting needed? [YES / NO]

"Ship quality. Move fast. Stay honest."

Speaker Timing Guide

Total meeting duration: 60 minutes (30 min reporting + 30 min discussion). Each speaker has a defined time allocation to ensure efficient coverage of all objectives while leaving room for collaborative problem-solving.

1	Title	CEO	0:30
2	Quarter Progress Overview	CEO	1:00
3	O1: What We Shipped	Charbel	3:00
4	O1: KR Dashboard	Jeff	2:00
5	O1: Quality Report	Vassili	3:00
6	O2: Progress Report	Vassili	2:00
7	O2: Axis Tracker	Vassili	3:00
8	O3: Pipeline Snapshot	CEO	3:00
9	O3: Deal Funnel & Activity	CEO	3:00
10	Red Flags & Risks	CEO	2:00
11	Action Plan	CEO	3:00
12	Closing	CEO	1:30

Pre-Meeting Prep Checklist

Each person must complete their assigned slides before the meeting begins. This ensures we spend meeting time on discussion and decision-making, not data entry or explanation of gaps. Coming prepared is non-negotiable.

Charbel

Slide 3: O1 shipped features, in progress work, and blockers

Jeff

Slide 4: All KR1.5 reliability metrics with current values

Vassili

Slides 5, 6, 7: Quality report, O2 progress, and axis tracker

CEO

Slides 8, 9, 10: Pipeline data, funnel distribution, red flag assessment

 **Critical rule:** If your slides aren't complete before the meeting, you present what you have and explain the gap.



ArcaScience

Seek less, discover better

ArcaScience, the new worldwide Benefit-Risk standard
